ID	Hide Row	Row Done	Task Name	Duration	Start	Finish	%	Rotante	Predecessors	Successo
0	**No**	**Yes**	**Proyecto**	**209.25 days?**	**Fri 9/27/24**	**Mon 6/30/25**	**0%**	**0 days?**		
1	No	Yes	1 Inicio del proyecto	0 days	Fri 9/27/24	Fri 9/27/24	0%	109.25 days		3
2										
3	**No**	**No**	**2 Pedido de Materiales**	**100 days**	**Fri 9/27/24**	**Mon 2/10/25**	**0%**	**109.25 days**	**1**	
4	No	No	2.1 Orden de Aceros	10 days	Fri 9/27/24	Wed 10/9/24	0%	199.25 days		
5	No	No	2.2 Compra de Equipos Promotor	100 days	Fri 9/27/24	Mon 2/10/25	0%	109.25 days		
6	No	No	2.3 Ordenar Tejas	30 days	Fri 9/27/24	Wed 11/6/24	0%	179.25 days		
7										
8	**No**	**No**	**3 Movimiento de Tierra**	**12.25 days**	**Fri 9/27/24**	**Sat 10/12/24**	**0%**	**2 days**		**109,163**
9	No	No	3.1 Corte y Excavacion	15 edays	Fri 9/27/24	Sat 10/12/24	0%	3.13 edays		
10										
11	No	No	4 Electricidad	150 days	Sat 10/12/24	Wed 4/30/25	0%	47 days	8	
12										
13	**No**	**No**	**5 Plomeria**	**150 days**	**Sat 10/12/24**	**Wed 4/30/25**	**0%**	**47 days**	**8**	
14	No	No	5.1 General	150 days	Sat 10/12/24	Wed 4/30/25	0%	47 days		
15	No	No	5.2 Recirculacion y Bordes infinitos heave	7 days	Fri 2/14/25	Mon 2/24/25	0%	98 days	241	
16										
17	**No**	**No**	**6 Tuneles y Pergolas**	**90 days**	**Sat 10/12/24**	**Wed 2/12/25**	**0%**	**107 days**	**8**	
18	No	No	6.1 Tuneles y Pergolas	90 days	Sat 10/12/24	Wed 2/12/25	0%	107 days		
19										
20										
21	**No**	**No**	**7 Mat Fondo Piscina de Sal (N -4.40)**	**13 days**	**Mon 10/28/24**	**Fri 11/15/24**	**0%**	**165 days**	**36**	
22	No	No	7.1 Excavacion Piscina de Sal	3 days	Mon 10/28/24	Thu 10/31/24	0%	165 days		23
23	No	No	7.2 Barrera de Vapor	0 days	Thu 10/31/24	Thu 10/31/24	0%	165 days	22	24
24	No	Yes	7.3 Conformado	2 days	Thu 10/31/24	Sat 11/2/24	0%	165 days	23	25
25	No	Yes	7.4 Formaleta	2 days	Sat 11/2/24	Thu 11/7/24	0%	165 days	24	26
26	No	No	7.5 Acero	3 days	Thu 11/7/24	Tue 11/12/24	0%	165 days	25	27
27	No	Yes	7.6 Hormigon (Xypex)	1 day	Tue 11/12/24	Wed 11/13/24	0%	165 days	26	28,30
28	No	No	7.7 Desencofre	2 days	Wed 11/13/24	Fri 11/15/24	0%	172 days	27	
29										
30	**No**	**No**	**8 Muro Piscina de Sal**	**9 days**	**Wed 11/13/24**	**Mon 11/25/24**	**0%**	**165 days**	**27**	
31	No	No	8.1 Acero	3 days	Wed 11/13/24	Mon 11/18/24	0%	165 days		32
32	No	No	8.2 Formaleta	3 days	Mon 11/18/24	Thu 11/21/24	0%	165 days	31	33
33	No	No	8.3 Hormigon (Xypex)	1 day	Thu 11/21/24	Fri 11/22/24	0%	165 days	32	34
34	No	No	8.4 Desencofre	2 days	Fri 11/22/24	Mon 11/25/24	0%	165 days	33	
35										
36	**No**	**No**	**9 Mat N -3.35 y N -3.40**	**12 days**	**Sat 10/12/24**	**Mon 10/28/24**	**0%**	**2 days**	**8**	**21**
37	No	No	9.1 Barrera de Vapor	0 days	Sat 10/12/24	Sat 10/12/24	0%	2 days		38
38	No	Yes	9.2 Conformado	2 days	Sat 10/12/24	Tue 10/15/24	0%	2 days	37	39
39	No	Yes	9.3 Formaleta	2 days	Tue 10/15/24	Thu 10/17/24	0%	2 days	38	40
40	No	No	9.4 Acero	5 days	Thu 10/17/24	Wed 10/23/24	0%	2 days	39	41
41	No	Yes	9.5 Hormigon	1 day	Wed 10/23/24	Thu 10/24/24	0%	2 days	40	42,52,44
42	No	No	9.6 Desencofre	2 days	Thu 10/24/24	Mon 10/28/24	0%	165 days	41	
43										
44	**No**	**No**	**10 columnas N -3.40 y N -3.35**	**16 days**	**Thu 10/24/24**	**Mon 11/18/24**	**0%**	**171 days**	**41**	
45	No	No	10.1 Replanteo	2 days	Thu 10/24/24	Mon 10/28/24	0%	171 days		46
46	No	No	10.2 Acero	4 days	Mon 10/28/24	Fri 11/1/24	0%	171 days	45	47
47	No	No	10.3 Formaleta	3 days	Fri 11/1/24	Thu 11/7/24	0%	171 days	46	48
48	No	No	10.4 Hormigon	2 days	Thu 11/7/24	Sat 11/9/24	0%	171 days	47	49
49	No	No	10.5 Desencofre	1 day	Sat 11/9/24	Tue 11/12/24	0%	171 days	48	50
50	No	No	10.6 Repello	4 days	Tue 11/12/24	Mon 11/18/24	0%	171 days	49	
51										
52	**No**	**No**	**11 Muro a N -1.50 (Eje 1 a 4 + Escalera)**	**12 days**	**Thu 10/24/24**	**Tue 11/12/24**	**0%**	**2 days**	**41**	**62,59**
53	No	No	11.1 Acero	5 days	Thu 10/24/24	Thu 10/31/24	0%	2 days		54
54	No	No	11.2 Waterstop	0 days	Thu 10/31/24	Thu 10/31/24	0%	2 days	53	55
55	No	No	11.3 Formaleta	5 days	Thu 10/31/24	Fri 11/8/24	0%	2 days	54	56
56	No	No	11.4 Hormigon	1 day	Fri 11/8/24	Sat 11/9/24	0%	2 days	55	57
57	No	No	11.5 Desencofre	1 day	Sat 11/9/24	Tue 11/12/24	0%	2 days	56	
58										
59	**No**	**No**	**12 Backfill y Compactacion**	**4 days**	**Tue 11/12/24**	**Mon 11/18/24**	**0%**	**171 days**	**52**	
60	No	No	12.1 Relleno y Compactacion	4 days	Tue 11/12/24	Mon 11/18/24	0%	171 days		
61										
62	**No**	**No**	**13 Mat Jacuzzi**	**7 days**	**Tue 11/12/24**	**Thu 11/21/24**	**0%**	**2 days**	**52**	
63	No	No	13.1 Barrera de Vapor	0 days	Tue 11/12/24	Tue 11/12/24	0%	2 days		64
64	No	Yes	13.2 Conformado	1 day	Tue 11/12/24	Wed 11/13/24	0%	2 days	63	65
65	No	Yes	13.3 Formaleta	2 days	Wed 11/13/24	Fri 11/15/24	0%	2 days	64	66
66	No	No	13.4 Acero	2 days	Fri 11/15/24	Tue 11/19/24	0%	2 days	65	67
67	No	Yes	13.5 Hormigon (Xypex)	1 day	Tue 11/19/24	Wed 11/20/24	0%	2 days	66	68,70
68	No	No	13.6 Desencofre	1 day	Wed 11/20/24	Thu 11/21/24	0%	168 days	67	
69										
70	**No**	**No**	**14 Muro Sobre Jacuzzi**	**6 days**	**Wed 11/20/24**	**Wed 11/27/24**	**0%**	**2 days**	**67**	**76**
71	No	No	14.1 Acero	2 days	Wed 11/20/24	Fri 11/22/24	0%	2 days		72
72	No	No	14.2 Formaleta	2 days	Fri 11/22/24	Mon 11/25/24	0%	2 days	71	73
73	No	No	14.3 Hormigon (Xypex)	1 day	Mon 11/25/24	Tue 11/26/24	0%	2 days	72	74
74	No	No	14.4 Desencofre	1 day	Tue 11/26/24	Wed 11/27/24	0%	2 days	73	
75										
76	**No**	**No**	**15 Backfill y Compactacion**	**5 days**	**Wed 11/27/24**	**Wed 12/4/24**	**0%**	**2 days**	**70**	**79**
77	No	No	15.1 Relleno y Compactacion	5 days	Wed 11/27/24	Wed 12/4/24	0%	2 days		
78										
79	**No**	**No**	**16 Mat (N -1.50) Jacuzzi/Piscina Sal**	**10 days**	**Wed 12/4/24**	**Wed 12/18/24**	**0%**	**2 days**	**76**	**87**
80	No	No	16.1 Barrera de Vapor	0 days	Wed 12/4/24	Wed 12/4/24	0%	2 days		81
81	No	Yes	16.2 Conformado	2 days	Thu 12/5/24	Fri 12/6/24	0%	2 days	80	82
82	No	Yes	16.3 Formaleta	2 days	Sat 12/7/24	Wed 12/11/24	0%	2 days	81	83
83	No	No	16.4 Acero	3 days	Wed 12/11/24	Sat 12/14/24	0%	2 days	82	84
84	No	Yes	16.5 Hormigon	1 day	Sat 12/14/24	Mon 12/16/24	0%	2 days	83	85,90
85	No	No	16.6 Desencofre	2 days	Mon 12/16/24	Wed 12/18/24	0%	80 days	84	
86										
87	**No**	**No**	**17 Escalera 7**	**10 days**	**Wed 12/18/24**	**Fri 1/3/25**	**0%**	**80 days**	**79**	**308**
88	No	No	17.1 Escalera 7	10 days	Wed 12/18/24	Fri 1/3/25	0%	80 days		
89										
90	**No**	**No**	**18 columnas N -1.50 (3ra fase)**	**19 days**	**Mon 12/16/24**	**Tue 1/14/25**	**0%**	**2 days**	**84**	
91	No	No	18.1 Replanteo	2 days	Mon 12/16/24	Wed 12/18/24	0%	2 days		92
92	No	No	18.2 Acero	3 days	Wed 12/18/24	Tue 12/24/24	0%	2 days	91	93
93	No	No	18.3 Formaleta	3 days	Tue 12/24/24	Sat 12/28/24	0%	2 days	92	94
94	No	No	18.4 Hormigon	2 days	Sat 12/28/24	Tue 12/31/24	0%	2 days	93	95,102,2
95	No	No	18.5 Desencofre	2 days	Tue 12/31/24	Fri 1/3/25	0%	131 days	94	96,98,97
96	No	No	18.6 Repello	6 days	Fri 1/3/25	Mon 1/13/25	0%	132 days	95	
97	No	No	18.7 Capiteles	7 days	Fri 1/3/25	Tue 1/14/25	0%	131 days	95	
98	No	No	18.8 Pedestales	7 days	Fri 1/3/25	Tue 1/14/25	0%	131 days	95	
99										
100	**No**	**No**	**19 Losa Postensada N -2.25 y -2.45**	**41 days**	**Wed 12/11/24**	**Wed 2/5/25**	**0%**	**16 days**		
101	No	No	19.1 Pedido de Formaleteo	14 days	Wed 12/11/24	Tue 12/31/24	0%	140 days	102SF	
102	No	No	19.2 Formaleteo	10 days	Tue 12/31/24	Wed 1/15/25	0%	2 days	94,157	103FS-2
103	No	No	19.3 Acero	7 days	Mon 1/13/25	Tue 1/21/25	0%	2 days	102FS-2 days	104
104	No	No	19.4 Cables Postensados	2 days	Tue 1/21/25	Thu 1/23/25	0%	2 days	103	105
105	No	No	19.5 Hormigon (Impermeabilizante)	2 days	Thu 1/23/25	Sat 1/25/25	0%	2 days	104	106,236
106	No	No	19.6 Tempiado de Cables	3 days	Mon 1/27/25	Wed 1/29/25	0%	113 days	105	107
107	No	No	19.7 Desencofrado	5 days	Thu 1/30/25	Wed 2/5/25	0%	113 days	106	
108										
109	**No**	**No**	**20 Mat Area Termal/Crioterapia (N -2.70)**	**18 days**	**Sat 10/12/24**	**Wed 11/6/24**	**0%**	**2 days**	**8**	**144**
110	No	No	20.1 Barrera de Vapor	1 day	Sat 10/12/24	Mon 10/14/24	0%	2 days		111
111	No	Yes	20.2 Conformado	3 days	Mon 10/14/24	Thu 10/17/24	0%	2 days	110	112
112	No	Yes	20.3 Formaleta	3 days	Thu 10/17/24	Mon 10/21/24	0%	2 days	111	113
113	No	No	20.4 Acero	6 days	Mon 10/21/24	Tue 10/29/24	0%	2 days	112	114
114	No	Yes	20.5 Hormigon	3 days	Tue 10/29/24	Fri 11/1/24	0%	2 days	113	115,117
115	No	No	20.6 Desencofre	2 days	Fri 11/1/24	Wed 11/6/24	0%	160 days	114	
116										
117	**No**	**No**	**21 Muro Piscina de Area Termal/Crioterap**	**14 days**	**Fri 11/1/24**	**Fri 11/22/24**	**0%**	**2 days**	**114**	**133,130**
118	No	No	21.1 Acero	5 days	Fri 11/1/24	Sat 11/9/24	0%	2 days		119
119	No	No	21.2 Waterstop	0 days	Sat 11/9/24	Sat 11/9/24	0%	2 days	118	120
120	No	No	21.3 Formaleta	4 days	Sat 11/9/24	Fri 11/15/24	0%	2 days	119	121
121	No	No	21.4 Hormigon (Xypex)	3 days	Fri 11/15/24	Wed 11/20/24	0%	2 days	120	122
122	No	No	21.5 Desencofre	2 days	Wed 11/20/24	Fri 11/22/24	0%	2 days	121	
123										
124	**No**	**No**	**22 Muro Piscina Sobre Rampa**	**13 days**	**Fri 11/1/24**	**Thu 11/21/24**	**0%**	**168 days**	**114**	
125	No	No	22.1 Acero	3 days	Fri 11/1/24	Thu 11/7/24	0%	171 days		126
126	No	No	22.2 Formaleta	3 days	Thu 11/7/24	Tue 11/12/24	0%	171 days	125	127
127	No	No	22.3 Hormigon (Xypex)	2 days	Fri 11/15/24	Tue 11/19/24	0%	168 days	20955,126	128
128	No	No	22.4 Desencofre	2 days	Tue 11/19/24	Thu 11/21/24	0%	168 days	127	
129										
130	**No**	**No**	**23 Escaleras 5 y 6**	**10 days**	**Fri 11/22/24**	**Thu 12/5/24**	**0%**	**99 days**	**117**	**308**
131	No	No	23.1 Escaleras	10 days	Fri 11/22/24	Thu 12/5/24	0%	99 days		
132										
133	**No**	**No**	**24 Backfill y Compactacion**	**5 days**	**Fri 11/22/24**	**Fri 11/29/24**	**0%**	**2 days**	**117**	**136**
134	No	No	24.1 Relleno y compactacion	5 days	Fri 11/22/24	Fri 11/29/24	0%	2 days		
135										
136	**No**	**No**	**25 Mat (N -1.50) Area Termal**	**16 days**	**Fri 11/29/24**	**Mon 12/23/24**	**0%**	**2 days**	**133**	
137	No	No	25.1 Barrera de Vapor	1 day	Fri 11/29/24	Sat 11/30/24	0%	2 days		138
138	No	Yes	25.2 Conformado	3 days	Mon 12/2/24	Wed 12/4/24	0%	2 days	137	139
139	No	Yes	25.3 Formaleta	3 days	Thu 12/5/24	Tue 12/10/24	0%	2 days	138	140
140	No	No	25.4 Acero	5 days	Tue 12/10/24	Mon 12/16/24	0%	2 days	139	141
141	No	Yes	25.5 Hormigon	2 days	Mon 12/16/24	Wed 12/18/24	0%	2 days	140	142,153
142	No	No	25.6 Desencofre	2 days	Wed 12/18/24	Mon 12/23/24	0%	146 days	141	
143										
144	**No**	**No**	**26 columnas N -2.70**	**19 days**	**Wed 11/6/24**	**Mon 12/2/24**	**0%**	**160 days**	**109**	
145	No	No	26.1 Replanteo	3 days	Wed 11/6/24	Sat 11/9/24	0%	160 days		146
146	No	No	26.2 Acero	3 days	Sat 11/9/24	Thu 11/14/24	0%	160 days	145	147
147	No	No	26.3 Formaleta	3 days	Thu 11/14/24	Tue 11/19/24	0%	160 days	146	148
148	No	No	26.4 Hormigon	2 days	Tue 11/19/24	Thu 11/21/24	0%	160 days	147	149
149	No	No	26.5 Desencofre	1 day	Thu 11/21/24	Fri 11/22/24	0%	160 days	148	150,151
150	No	No	26.6 Repello	6 days	Fri 11/22/24	Sat 11/30/24	0%	161 days	149	
151	No	No	26.7 Capiteles	7 days	Fri 11/22/24	Mon 12/2/24	0%	160 days	149	
152										
153	**No**	**No**	**27 columnas N -1.50 (2da fase)**	**17 days**	**Wed 12/18/24**	**Tue 1/14/25**	**0%**	**2 days**	**141**	
154	No	No	27.1 Replanteo	2 days	Wed 12/18/24	Mon 12/23/24	0%	2 days		155
155	No	No	27.2 Acero	2 days	Mon 12/23/24	Thu 12/26/24	0%	2 days	154	156
156	No	No	27.3 Formaleta	3 days	Thu 12/26/24	Mon 12/30/24	0%	2 days	155	157
157	No	No	27.4 Hormigon	1 day	Mon 12/30/24	Tue 12/31/24	0%	2 days	156	158,102
158	No	No	27.5 Desencofre	2 days	Tue 12/31/24	Fri 1/3/25	0%	131 days	157	159,161
159	No	No	27.6 Repello	3 days	Fri 1/3/25	Tue 1/7/25	0%	135 days	158	
160	No	No	27.7 Capiteles	7 days	Fri 1/3/25	Tue 1/14/25	0%	131 days	158	
161	No	No	27.8 Pedestales	7 days	Fri 1/3/25	Tue 1/14/25	0%	131 days	158	
162										
163	**No**	**No**	**28 Mat (N -1.50) separado a 1.5mts de m**	**22 days**	**Sat 10/12/24**	**Tue 11/12/24**	**0%**	**57 days**	**8**	**171,260**
164	No	No	28.1 Barrera de Vapor	1 day	Sat 10/12/24	Mon 10/14/24	0%	57 days		165
165	No	Yes	28.2 Conformado	3 days	Mon 10/14/24	Thu 10/17/24	0%	57 days	164	166
166	No	Yes	28.3 Formaleta	3 days	Thu 10/17/24	Mon 10/21/24	0%	57 days	165	167
167	No	No	28.4 Acero	10 days	Mon 10/21/24	Sat 11/2/24	0%	57 days	166	168
168	No	Yes	28.5 Hormigon	3 days	Sat 11/2/24	Fri 11/8/24	0%	57 days	167	169
169	No	No	28.6 Desencofre	2 days	Fri 11/8/24	Tue 11/12/24	0%	57 days	168	

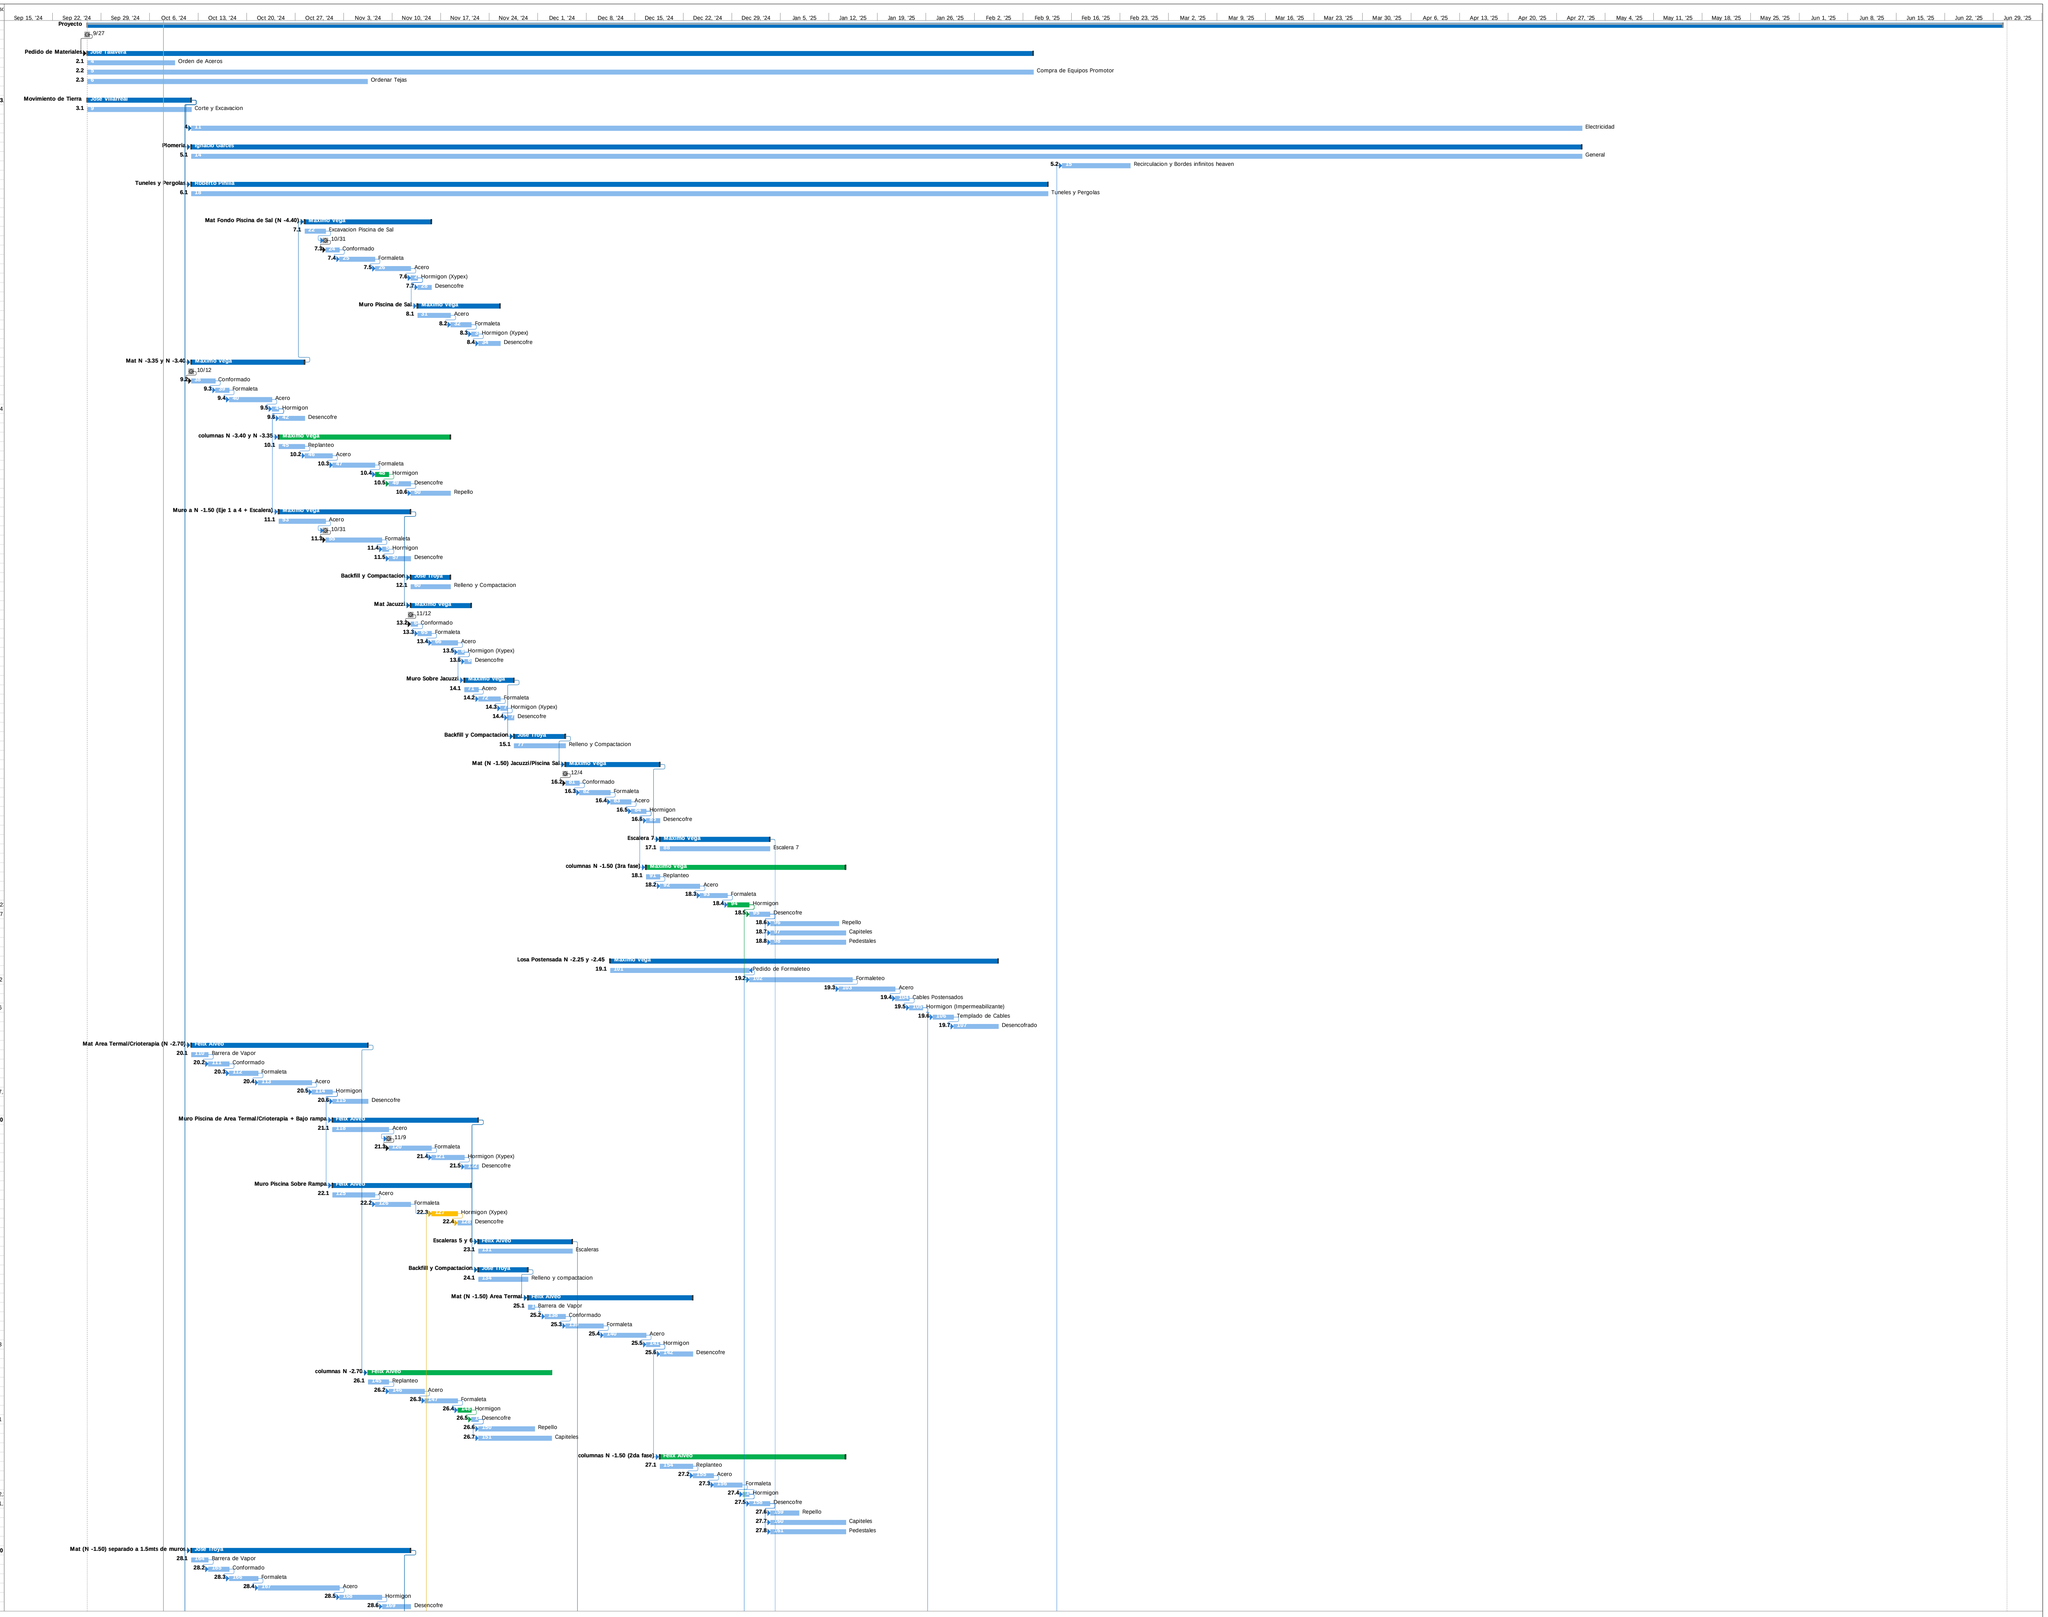

Project: Proyecto
Date: Tue 10/8/24

Task | Split | Milestone | Summary | Project Summary | Inactive Task | Inactive Milestone | Inactive Summary | Manual Task | Duration-only | Manual Summary Rollup | Manual Summary | Start-only | Finish-only | External Tasks | External Milestone | Deadline | Critical | Critical Split | Progress | Manual Progress

ID	Hide Row	Row Done	Task Name	Duration	Start	Finish	%	Rotante	Predecessors	Successo
170										
171	**No**	**No**	**29 columnas N -1.50 (1ra fase)**	**36 days**	**Tue 11/12/24**	**Thu 1/2/25**	**0%**	**57 days**	**163**	
172	No	No	29.1 Replanteo	3 days	Tue 11/12/24	Fri 11/15/24	0%	57 days		173
173	No	No	29.2 Acero	7 days	Fri 11/15/24	Mon 11/25/24	0%	57 days	172	174
174	No	No	29.3 Formaleta	10 days	Mon 11/25/24	Tue 12/10/24	0%	57 days	173	175
175	No	No	29.4 Hormigon	5 days	Tue 12/10/24	Mon 12/16/24	0%	57 days	174	176
176	No	No	29.5 Desencofre	3 days	Mon 12/16/24	Thu 12/19/24	0%	57 days	175	177,179,
177	No	No	29.6 Repello	8 days	Thu 12/19/24	Thu 1/2/25	0%	139 days	176	
178	No	No	29.7 Capiteles	7 days	Thu 12/19/24	Tue 12/31/24	0%	140 days	176	
179	No	No	29.8 Pedestales	7 days	Thu 12/19/24	Tue 12/31/24	0%	140 days	176	
180										
181	**No**	**No**	**30 Muro 4**	**12 days**	**Thu 12/19/24**	**Tue 1/7/25**	**0%**	**57 days**	**176**	**187**
182	No	No	30.1 Acero	3 days	Thu 12/19/24	Thu 12/26/24	0%	57 days		183
183	No	No	30.2 Formaleta	5 days	Thu 12/26/24	Thu 1/2/25	0%	57 days	182	184
184	No	No	30.3 Hormigon	2 days	Thu 1/2/25	Sat 1/4/25	0%	57 days	183	185
185	No	No	30.4 Desencofre	2 days	Sat 1/4/25	Tue 1/7/25	0%	57 days	184	
186										
187	**No**	**No**	**31 Escaleras 1 y 2**	**20 days**	**Tue 1/7/25**	**Mon 2/3/25**	**0%**	**57 days**	**181**	**308**
188	No	No	31.1 Escalera 1 (Espejismo)	10 days	Tue 1/7/25	Tue 1/21/25	0%	57 days		189
189	No	No	31.2 Escalera 2 (Sobre piscina termal)	10 days	Tue 1/21/25	Mon 2/3/25	0%	57 days	188	
190										
191	**No**	**No**	**32 Muro 6 (bajo rampa) y 7**	**15 days?**	**Sat 10/12/24**	**Thu 10/31/24**	**0%**	**116 days?**	**8**	**205**
192	No	No	32.1 Acero	4 days	Sat 10/12/24	Thu 10/17/24	0%	116 days		193
193	No	No	32.2 Waterstop	1 day?	Thu 10/17/24	Fri 10/18/24	0%	116 days?	192	194
194	No	No	32.3 Formaleta	6 days	Fri 10/18/24	Fri 10/25/24	0%	116 days	193	195
195	No	No	32.4 Hormigon	2 days	Fri 10/25/24	Tue 10/29/24	0%	116 days	194	196,203
196	No	No	32.5 Desencofre	2 days	Tue 10/29/24	Thu 10/31/24	0%	116 days	195	
197										
198	**No**	**No**	**33 Mat y Rampa de Playa (Xypex)**	**15 days**	**Sat 10/12/24**	**Thu 10/31/24**	**0%**	**116 days**	**8**	
199	No	No	33.1 Barrera de Vapor	1 day	Sat 10/12/24	Mon 10/14/24	0%	117 days		200
200	No	Yes	33.2 Conformado	2 days	Mon 10/14/24	Wed 10/16/24	0%	117 days	199	201
201	No	Yes	33.3 Formaleta	3 days	Wed 10/16/24	Sat 10/19/24	0%	117 days	200	202
202	No	No	33.4 Acero	6 days	Sat 10/19/24	Mon 10/28/24	0%	117 days	201	203
203	No	Yes	33.5 Hormigon (Xypex)	2 days	Tue 10/29/24	Thu 10/31/24	0%	116 days	202,195	205
204										
205	**No**	**No**	**34 Muro 5, 6 (sobre rampa) y Muro 10/503 (Xypex)**	**14 days**	**Thu 10/31/24**	**Thu 11/21/24**	**0%**	**116 days**	**203,191**	**212**
206	No	No	34.1 Acero	4 days	Thu 10/31/24	Thu 11/7/24	0%	116 days		207
207	No	No	34.2 Waterstop	1 day	Thu 11/7/24	Fri 11/8/24	0%	116 days	206	208
208	No	No	34.3 Formaleta	5 days	Fri 11/8/24	Fri 11/15/24	0%	116 days	207	209
209	No	No	34.4 Hormigon (Xypex)	2 days	Fri 11/15/24	Tue 11/19/24	0%	116 days	208	210,1275
210	No	No	34.5 Desencofre	2 days	Tue 11/19/24	Thu 11/21/24	0%	116 days	209	
211										
212	**No**	**No**	**35 Muro 9/503**	**15 days**	**Thu 11/21/24**	**Thu 12/12/24**	**0%**	**116 days**	**205**	**222,218**
213	No	No	35.1 Acero	4 days	Thu 11/21/24	Tue 11/26/24	0%	116 days		214
214	No	No	35.2 Formaleta	7 days	Tue 11/26/24	Thu 12/5/24	0%	116 days	213	215
215	No	No	35.3 Hormigon	2 days	Fri 12/6/24	Tue 12/10/24	0%	116 days	214	216
216	No	No	35.4 Desencofre	2 days	Tue 12/10/24	Thu 12/12/24	0%	116 days	215	
217										
218	**No**	**No**	**36 Escaleras 3 y 4**	**17 days**	**Thu 12/12/24**	**Mon 1/6/25**	**0%**	**136 days**	**212**	
219	No	No	36.1 Escaleras 4 (Hacia Cuarto Electrico)	7 days	Thu 12/12/24	Mon 12/23/24	0%	136 days		220
220	No	No	36.2 Escalera 3 (En terraza)	10 days	Mon 12/23/24	Mon 1/6/25	0%	136 days	219	
221										
222	**No**	**No**	**37 Backfill Playa**	**10 days**	**Thu 12/12/24**	**Fri 12/27/24**	**0%**	**116 days**	**212**	
223	No	No	37.1 Relleno Terraza	5 days	Thu 12/12/24	Wed 12/18/24	0%	116 days		224,226
224	No	No	37.2 Relleno Fuera Muro	5 days	Wed 12/18/24	Fri 12/27/24	0%	143 days	223	
225										
226	**No**	**No**	**38 Cuarto Electrico**	**32 days**	**Wed 12/18/24**	**Fri 1/31/25**	**0%**	**116 days**	**223**	
227	No	No	38.1 Zapatas y Columnas	7 days	Wed 12/18/24	Mon 12/30/24	0%	116 days		228
228	No	No	38.2 Piso	5 days	Mon 12/30/24	Mon 1/6/25	0%	116 days	227	229
229	No	No	38.3 Paredes	10 days	Mon 1/6/25	Mon 1/20/25	0%	116 days	228	230
230	No	No	38.4 Losa	10 days	Mon 1/20/25	Fri 1/31/25	0%	116 days	229	
231										
232	**No**	**No**	**39 Losa Postensada N -2.70**	**49 days**	**Wed 12/11/24**	**Fri 2/14/25**	**0%**	**20 days**		**290**
233	No	No	39.1 Pedido de Formaleteo	14 days	Wed 12/11/24	Tue 12/31/24	0%	97 days	234SF	
234	No	No	39.2 Formaleteo	10 days	Tue 12/31/24	Wed 1/15/25	0%	6 days	94,157	235SF,23
235	No	No	39.3 Acero 1a fase	7 days	Mon 1/13/25	Tue 1/21/25	0%	6 days	234FS-2 days	236
236	No	No	39.4 Styropor	2 days	Mon 1/27/25	Tue 1/28/25	0%	2 days	235,135	237
237	No	No	39.5 Acero 2da fase	5 days	Wed 1/29/25	Tue 2/4/25	0%	2 days	236	238
238	No	No	39.6 Cables Postensados	3 days	Tue 2/4/25	Fri 2/7/25	0%	2 days	237	239
239	No	No	39.7 Hormigon	2 days	Fri 2/7/25	Mon 2/10/25	0%	2 days	238	240,243
240	No	No	39.8 Templado de Cables	3 days	Mon 2/10/25	Thu 2/13/25	0%	2 days	239	241,267,
241	No	No	39.9 Desencofrado	1 day	Thu 2/13/25	Fri 2/14/25	0%	2 days	240	251,153,
242										
243	**No**	**No**	**40 Asientos y Muros VIP**	**10 days**	**Mon 2/10/25**	**Sat 2/22/25**	**0%**	**99 days**	**239**	
244	No	No	40.1 Asientos y Muros	10 days	Mon 2/10/25	Sat 2/22/25	0%	99 days		
245										
246	**No**	**No**	**41 Sobrepiso N -2.45**	**6 days**	**Thu 3/27/25**	**Thu 4/3/25**	**0%**	**68 days**	**275**	
247	No	No	41.1 Styropor	2 days	Thu 3/27/25	Fri 3/28/25	0%	68 days		248
248	No	No	41.2 Acero	2 days	Sat 3/29/25	Tue 4/1/25	0%	68 days	247	249
249	No	No	41.3 Hormigon	2 days	Tue 4/1/25	Thu 4/3/25	0%	68 days	248	
250										
251	**No**	**No**	**42 Vigas Invertidas**	**22 days**	**Fri 2/14/25**	**Sat 3/15/25**	**0%**	**51.13 days**	**241**	**257FS-1**
252	No	No	42.1 Formaleta	9 days	Fri 2/14/25	Wed 2/26/25	0%	51.13 days		253
253	No	No	42.2 acero	9 days	Wed 2/26/25	Tue 3/11/25	0%	51.13 days	252	254
254	No	No	42.3 hormigon	2 days	Tue 3/11/25	Thu 3/13/25	0%	51.13 days	253	255
255	No	No	42.4 desencofre	2 days	Thu 3/13/25	Sat 3/15/25	0%	51.13 days	254	
256										
257	**No**	**No**	**43 Bovedas**	**47 days**	**Mon 2/24/25**	**Fri 4/25/25**	**0%**	**51 days**	**251FS-15 da**	
258	No	No	43.1 Bovedas	60 edays	Mon 2/24/25	Fri 4/25/25	0%	65.88 edays		
259										
260	**No**	**No**	**44 Paredes PB**	**73 days**	**Tue 11/12/24**	**Wed 2/19/25**	**0%**	**72 days**	**163**	
261	No	No	44.1 Replanteo	5 days	Tue 11/12/24	Tue 11/19/24	0%	72 days		262
262	No	No	44.2 Bloqueo	30 days	Tue 11/19/24	Tue 12/31/24	0%	72 days	261	263FS-2
263	No	No	44.3 Repello	45 days	Fri 11/29/24	Thu 1/30/25	0%	72 days	262FS-22 days	264
264	No	No	44.4 Filos y mochetas	15 days	Fri 1/31/25	Wed 2/19/25	0%	72 days	263	297
265										
266	**No**	**No**	**45 Paredes Heaven**	**25 days**	**Thu 2/13/25**	**Tue 3/18/25**	**0%**	**54 days**		**275,272**
267	No	No	45.1 Replanteo	2 days	Thu 2/13/25	Mon 2/17/25	0%	54 days	240	268
268	No	No	45.2 Bloqueo	10 days	Mon 2/17/25	Fri 2/28/25	0%	54 days	267	269
269	No	No	45.3 Repello	10 days	Fri 2/28/25	Fri 3/14/25	0%	54 days	268	270,304
270	No	No	45.4 Filos y mochetas	3 days	Fri 3/14/25	Tue 3/18/25	0%	54 days	269	313,299
271										
272	**No**	**No**	**46 Columnas PA**	**12 days**	**Thu 2/13/25**	**Fri 2/28/25**	**0%**	**0 days**	**266ES**	
273	No	No	46.1 Columnas de Techo	12 days	Thu 2/13/25	Fri 2/28/25	0%	0 days		278
274										
275	**No**	**No**	**47 Impermeabilizacion Superficial**	**7 days**	**Tue 3/18/25**	**Wed 3/26/25**	**0%**	**54 days**	**266**	**246,294**
276	No	No	47.1 Impermeabilizacion Superficial	7 days	Tue 3/18/25	Wed 3/26/25	0%	54 days		
277										
278	**No**	**No**	**48 Techos**	**29 days**	**Fri 2/28/25**	**Mon 4/7/25**	**0%**	**0 days**	**273**	
279	No	No	48.1 Vigas	7 days	Fri 2/28/25	Tue 3/11/25	0%	0 days		280
280	No	No	48.2 Carriolas	7 days	Tue 3/11/25	Wed 3/19/25	0%	0 days	279	281
281	No	No	48.3 Aislante	1 day	Wed 3/19/25	Thu 3/20/25	0%	0 days	280	282
282	No	No	48.4 Tejalit	7 days	Thu 3/20/25	Fri 3/28/25	0%	0 days	281	283,285
283	No	No	48.5 Tejas	7 days	Sat 3/29/25	Mon 4/7/25	0%	65 days	282	
284										
285	**No**	**No**	**49 Cielorraso**	**11 days**	**Sat 3/29/25**	**Fri 4/11/25**	**0%**	**0 days**	**282**	
286	No	No	49.1 estructura	5 days	Sat 3/29/25	Fri 4/4/25	0%	0 days		287
287	No	No	49.2 laminas (coloc. pasteo y lijado)	5 days	Fri 4/4/25	Thu 4/10/25	0%	0 days	286	288,315
288	No	No	49.3 Sellado	1 day	Thu 4/10/25	Fri 4/11/25	0%	58 days	287	300
289										
290	No	No	50 Losa Pasteada (Area 9.10,11,12 y pasillo)	15 days	Fri 2/14/25	Thu 3/6/25	0%	62 days	232	292FS-7
291										
292	**No**	**No**	**51 Revestimiento**	**43 days**	**Tue 2/25/25**	**Tue 4/22/25**	**0%**	**54 days**	**290FS-7 day**	
293	No	No	51.1 Baldosas de Piso y Paredes PB	35 days	Tue 2/25/25	Thu 4/10/25	0%	62 days		
294	No	No	51.2 Baldosas de Piso y Paredes PA	20 days	Thu 3/27/25	Tue 4/22/25	0%	54 days	275	
295										
296	**No**	**No**	**52 Pintura**	**44 days**	**Wed 2/19/25**	**Wed 4/16/25**	**0%**	**58 days**		
297	No	No	52.1 Paredes PB	30 days	Wed 2/19/25	Fri 3/28/25	0%	72 days	264	
298	No	No	52.2 Losa vista PB	7 days	Thu 3/6/25	Sat 3/15/25	0%	83 days	290	
299	No	No	52.3 Paredes PA	7 days	Tue 3/18/25	Wed 3/26/25	0%	74 days	270	
300	No	No	52.4 Cielo de Gypsum	3 days	Fri 4/11/25	Wed 4/16/25	0%	58 days	288	
301										
302	**No**	**No**	**53 Vidrios**	**70 days**	**Thu 12/26/24**	**Wed 3/26/25**	**0%**	**74 days**		
303	No	No	53.1 Pedido de Vidrios	60 days	Thu 12/26/24	Fri 3/14/25	0%	84 days	304SF	
304	No	No	53.2 Instalacion de Vidrios	10 days	Fri 3/14/25	Wed 3/26/25	0%	74 days	269	303SF
305										
306	**No**	**No**	**54 Barandas**	**70 days**	**Sat 11/23/24**	**Wed 2/26/25**	**0%**	**48 days**		**332**
307	No	No	54.1 Pedido de Barandas	60 days	Sat 11/23/24	Thu 2/13/25	0%	58 days	309SF,308SF	
308	No	No	54.2 Instalacion de Barandas	10 days	Thu 2/13/25	Wed 2/26/25	0%	48 days	240,87,130,18	307SF
309	No	No	54.3 Instalacion de Pasamanos	10 days	Thu 2/13/25	Wed 2/26/25	0%	48 days	240	307SF
310										
311	**No**	**No**	**55 Puertas**	**75 days**	**Mon 12/30/24**	**Sat 4/5/25**	**0%**	**66 days**		
312	No	No	55.1 Pedido de Puertas	60 days	Mon 12/30/24	Tue 3/18/25	0%	81 days	313SF	
313	No	No	55.2 Instalacion de Puertas	15 days	Tue 3/18/25	Sat 4/5/25	0%	66 days	270	312SF
314										
315	**No**	**No**	**56 Alarma Contra Incendio**	**14 days**	**Thu 4/10/25**	**Tue 4/29/25**	**0%**	**0 days**	**287**	
316	No	No	56.1 Instalacion de detectores y Panel	14 days	Thu 4/10/25	Tue 4/29/25	0%	0 days		333
317										
318	**No**	**No**	**57 HVAC**	**51 days**	**Tue 1/7/25**	**Fri 3/14/25**	**0%**	**84 days**		
319	No	No	57.1 Fabricacion	30 days	Tue 1/7/25	Fri 2/14/25	0%	105 days	320SF	
320	No	No	57.2 Ducteria	21 days	Fri 2/14/25	Fri 3/14/25	0%	84 days	241	319SF
321										
322	**No**	**No**	**58 Equipos**	**55 days**	**Fri 2/14/25**	**Sat 4/26/25**	**0%**	**2 days**	**241**	**332**
323	No	No	58.1 Montaje de equipos de piscina	55 days	Fri 2/14/25	Sat 4/26/25	0%	2 days		
324	No	No	58.2 Montaje de Aires	55 days	Fri 2/14/25	Sat 4/26/25	0%	2 days		
325	No	No	58.3 Montaje de Equipos de Sauna	55 days	Fri 2/14/25	Sat 4/26/25	0%	2 days		
326	No	No	58.4 Montaje de Generadores de Vapor	55 days	Fri 2/14/25	Sat 4/26/25	0%	2 days		
327	No	No	58.5 Montaje de Rejillas	55 days	Fri 2/14/25	Sat 4/26/25	0%	2 days		
328	No	No	58.6 Montaje de Trampas	55 days	Fri 2/14/25	Sat 4/26/25	0%	2 days		
329										
330	No	No	59 Señalizacion	14 days	Thu 4/10/25	Tue 4/29/25	0%	48 days	332SF	
331										
332	**No**	**No**	**60 Permisos**	**48 days**	**Tue 4/29/25**	**Mon 6/30/25**	**0%**	**0 days**	**322,306**	**330SF**
333	No	No	60.1 Permiso de Bomberos	24 days	Tue 4/29/25	Fri 5/30/25	0%	0 days	316	334
334	No	No	60.2 Permiso de Municipio	24 days	Fri 5/30/25	Mon 6/30/25	0%	0 days	333	

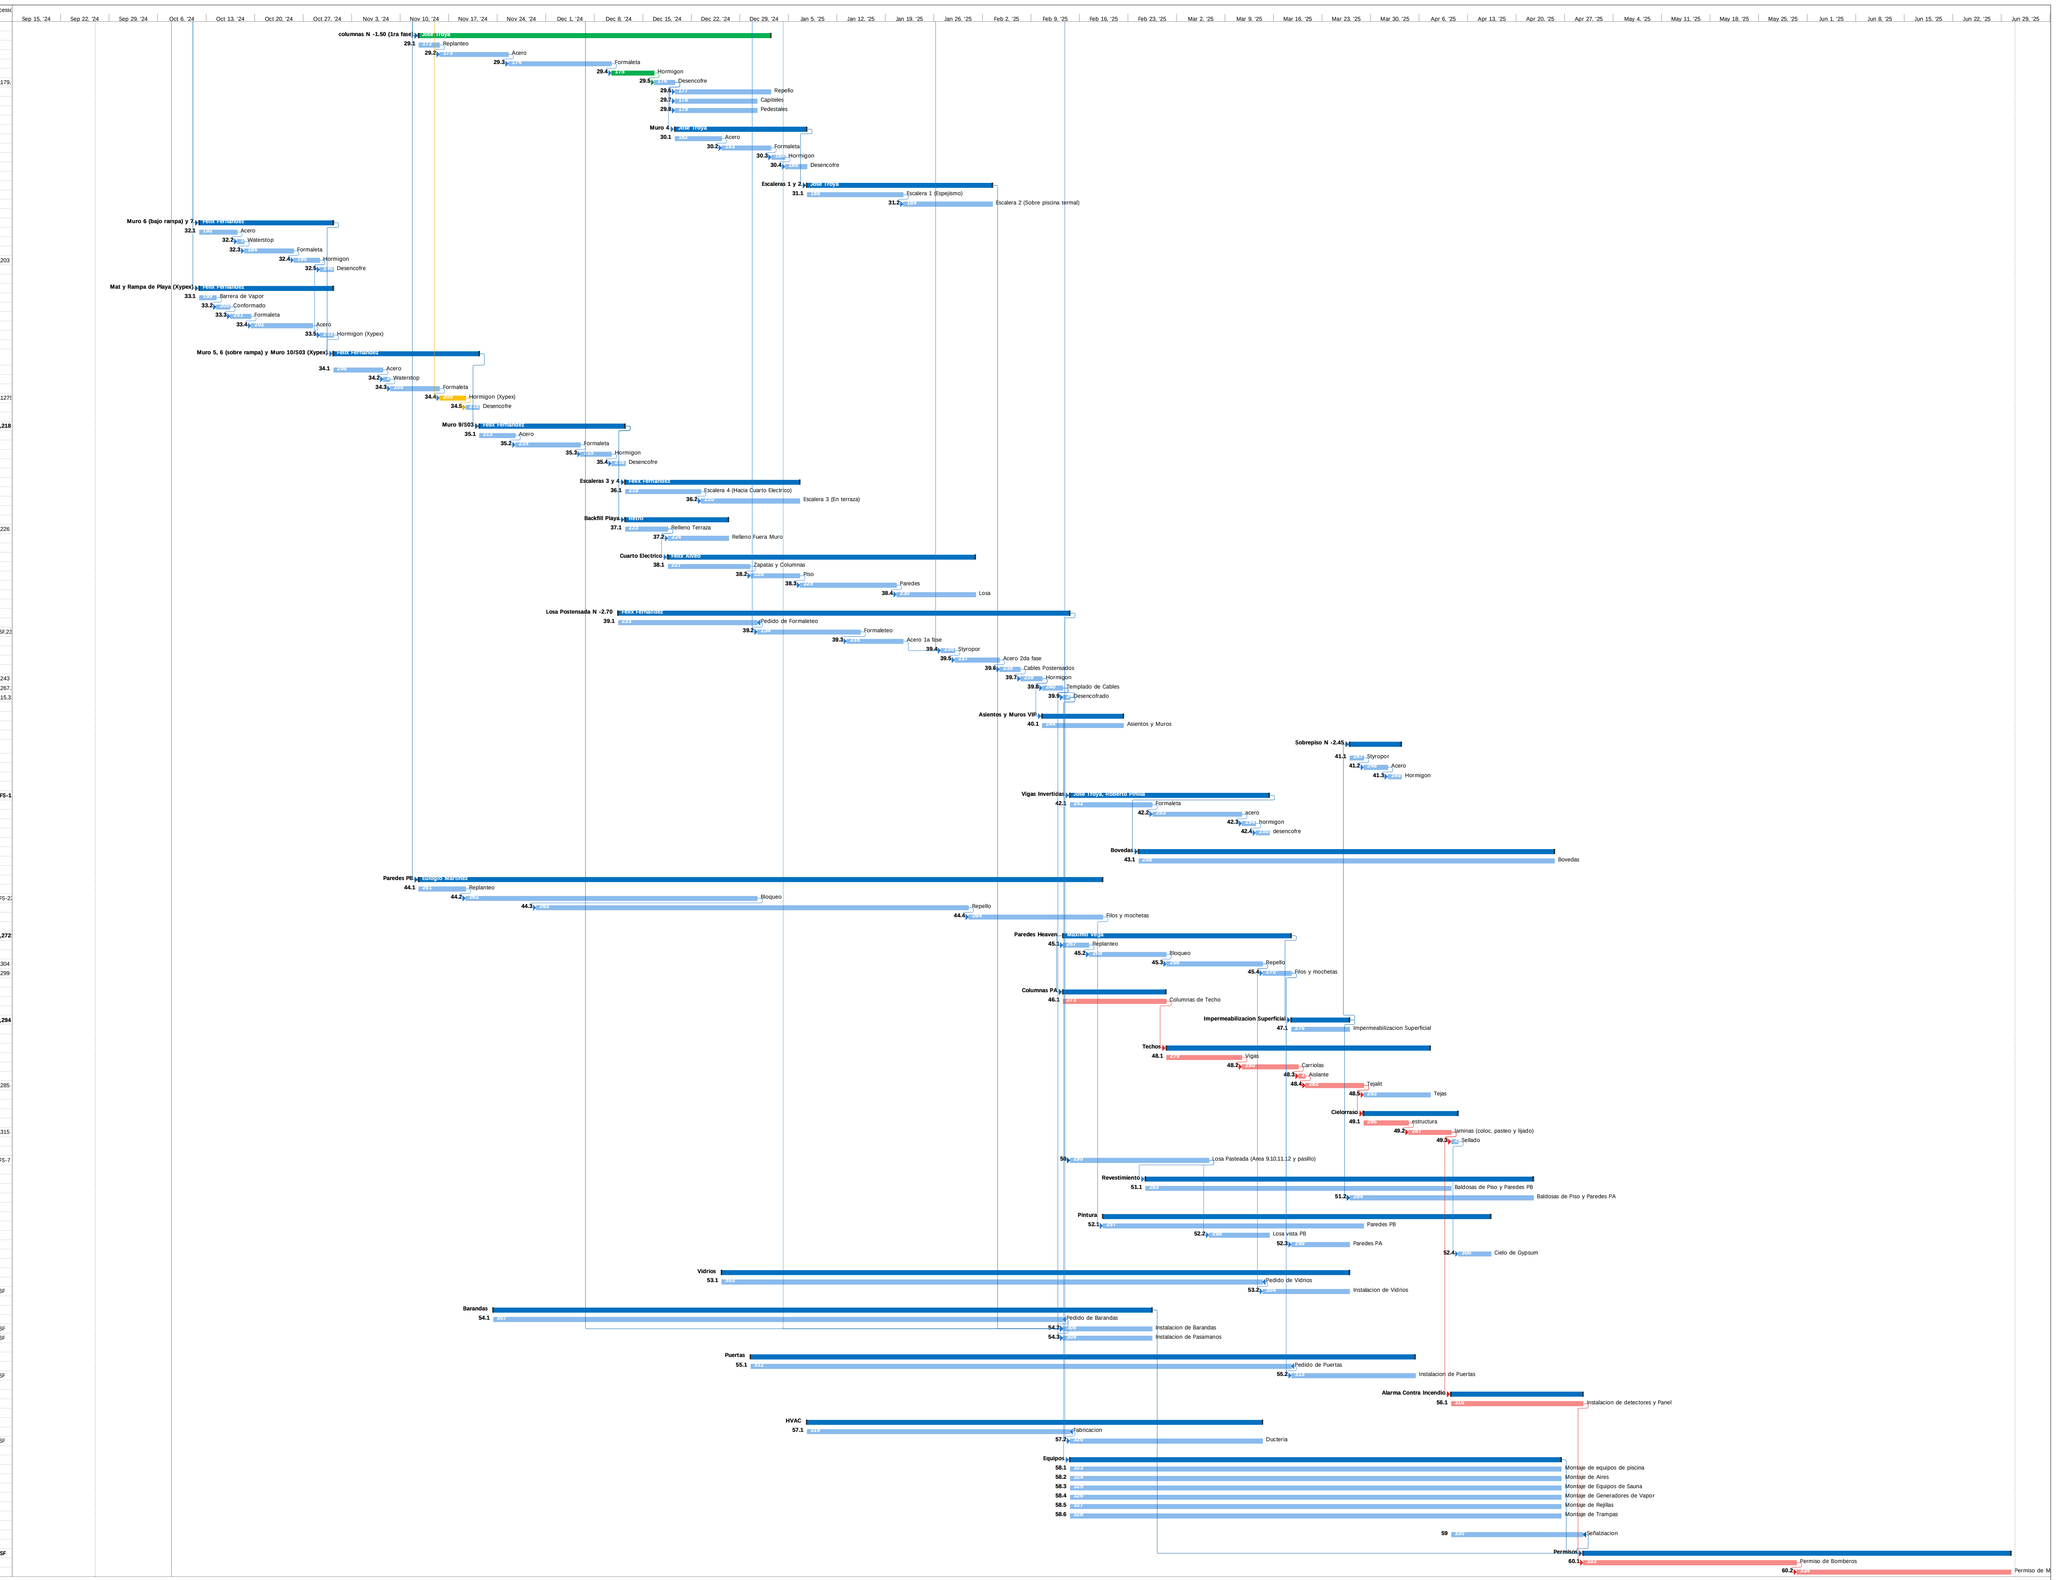

Project: Proyecto
Date: Tue 10/8/24

Task | Split | Milestone | Summary | Project Summary | Inactive Task | Inactive Milestone | Inactive Summary | Manual Task | Duration-only | Manual Summary Rollup | Manual Summary | Start-only | Finish-only | External Tasks | External Milestone | Deadline | Critical | Critical Split | Progress | Manual Progress
